Activity ID	Activity Name	Original Duration	Start	Finish
PSHIAInfield Utility Access Upgrades an		66d	22-Apr-24	25-Jul-24
A1000	Mobilization	0d	22-Apr-24*	
A1020	Verifiy Survey Control Points	1d	22-Apr-24	23-Apr-24
A1030	Saw Cut Existing Asphalt	4d	22-Apr-24	25-Apr-24
A1040	Remove Existing Cable	3d	22-Apr-24	24-Apr-24
A1011	Install SWPPP	1d	22-Apr-24	22-Apr-24
A1050	Remove & Salvage Exisitng Signs	4d	25-Apr-24	30-Apr-24
A1060	Demo Exisitng Concrete Sign Bases	4d	01-May-24	06-May-24
A1070	Trench for New Electrical Runs	3d	07-May-24	09-May-24
A1080	Install New Conduit	3d	10-May-24	14-May-24
A1090	Install New Sign Bases	4d	15-May-24	20-May-24
A1061	Remove & Salvage Vault Lids	13d	21-May-24	07-Jun-24
A1091	Install New Concrete Lid and Apron	10d	21-May-24	04-Jun-24
A1092	Adjust Utility Vaults	3d	05-Jun-24	07-Jun-24
A1110	Haul & Place Subgrade Material	10d	10-Jun-24	21-Jun-24
A1120	Subgrade Finegrade	10d	24-Jun-24	08-Jul-24
A1121	Remove Double Grate Catch Basin	2d	24-Jun-24	25-Jun-24
A1140	Install / Backfill, / & compact New Triple Grate	4d	26-Jun-24	01-Jul-24
A1130	Haul & Place P-403 Asphalt	9d	03-Jul-24	16-Jul-24
A1149	Pull Electrical Cable	2d	17-Jul-24	18-Jul-24
A1150	Install New Guidance Signs	3d	19-Jul-24	23-Jul-24
A1160	Install Manhole ID Plaques	1d	24-Jul-24	25-Jul-24
A1170	Project Complete	0d		25-Jul-24

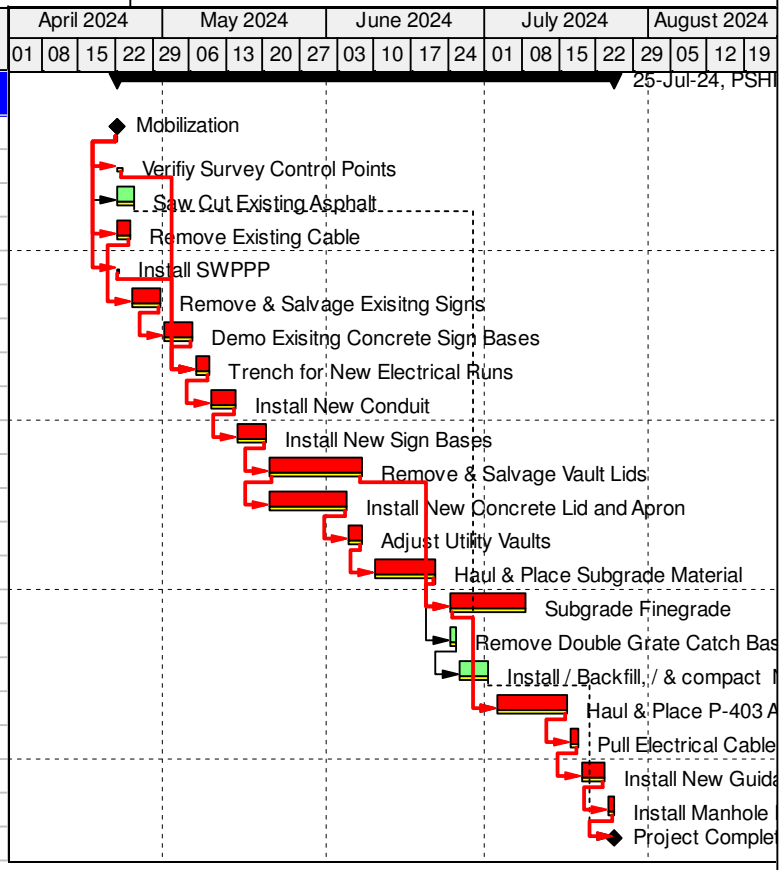

Project Baseline Bar | Remaining Work | Actual Work | Critical Remaining ...

TASK filter: All Activities

© Oracle Corporation
